

Bristol Town Administrator

From: Nick Morehouse <nmorehouse@aegis-re.com>
Sent: Friday, September 24, 2021 7:17 PM
To: Ben Marks; Bristol Town Administrator
Cc: Richard Carpenter; Greg Pahl; Tom Dunne; Susan Smiley; Peter Carothers; Richard Butz; Sally Burrell; Thomas Flynn; Eric Phaneuf; Nils Behn; Sonia Behn; Nick Morehouse; Eric Cota
Subject: Acorn Bristol Solar Project Status Report #4
Attachments: 2021-09-24_Acorn Bristol_Status_Report_#04.pdf; 2021-09-10_BristolLF_Schedule_Final_2.2.pdf

Hello Ben & Valerie,

Please find the latest status report & schedule attached.

We started receiving the steel today as planned and will begin construction next week, also as planned. I am including an updated schedule as last week's schedule was inadvertently overwritten with bad data.

Please let me know if you have any questions.

Thanks & have a great weekend,
Nick

Nick Morehouse
Senior Project Manager



Aegis Renewable Energy
, Inc.
340 Mad River Park, Suite 6
Waitsfield, VT 05673
Main: [802-496-5155](tel:802-496-5155)
Cell: [802-557-5240](tel:802-557-5240)



The information contained in this facsimile/email transmission is privileged and confidential and is intended only for the use of the recipient listed above. If you are neither the intended recipient or an employee or agent of the intended recipient responsible for the delivery of this information, you are hereby notified that the disclosure, copying, use or distribution of this information is strictly prohibited. If you have received this transmission in error, please notify us immediately to arrange for the return of the transmitted documents or to verify their destruction.



**Bristol 500 kW Ground Mount
Acorn Energy Solar 3, LLC.
Status Report 04
09/24/2021**

Acorn Bristol Solar

Scope Elements	Current Status	Action Items-Look Ahead's-Notes
Permitting	All permits are issued.	
General Conditions	Subcontractors have been selected	Need to finalize subcontract with electrician.
Site Work-Excavation		
Racking	Half of the racking was received this morning and transported to the lay down area.	Remaining steel to be delivered on 9/27 & 9/28. Assembly begins 9/28 with racking field trainer on-site.
Electrical Equipment Procurement		
Electrical Equipment (Med Dist)		
Electrical Install		
PV Modules	On-site	
Inverters		Conformed week of 9/27 delivery
Data Acquisition System (DAS)		
Fencing		
Project Commissioning – Mech Comp		
Utility Work- Interconnection		

Current Schedule Performance: 0% ±Complete...Current Schedule Version: 2021-09-10_BristolLF_Schedule_Final_2.2

Current Project Completion Date (WPS): 12/21/2021



Project Contacts:


Nick Morehouse
Sr. Project Manager
340 Mad River Park, Suite 6
Waitsfield, VT 05673

C: 802.557.5240
nmorehouse@aegis-re.com

Tom Flynn P.E.
COO
340 Mad River Park, Suite 6
Waitsfield, VT 05673

O: 802.496.5155
C: 617-694-8464
tflynn@aegis-re.com

www.aegis-re.com

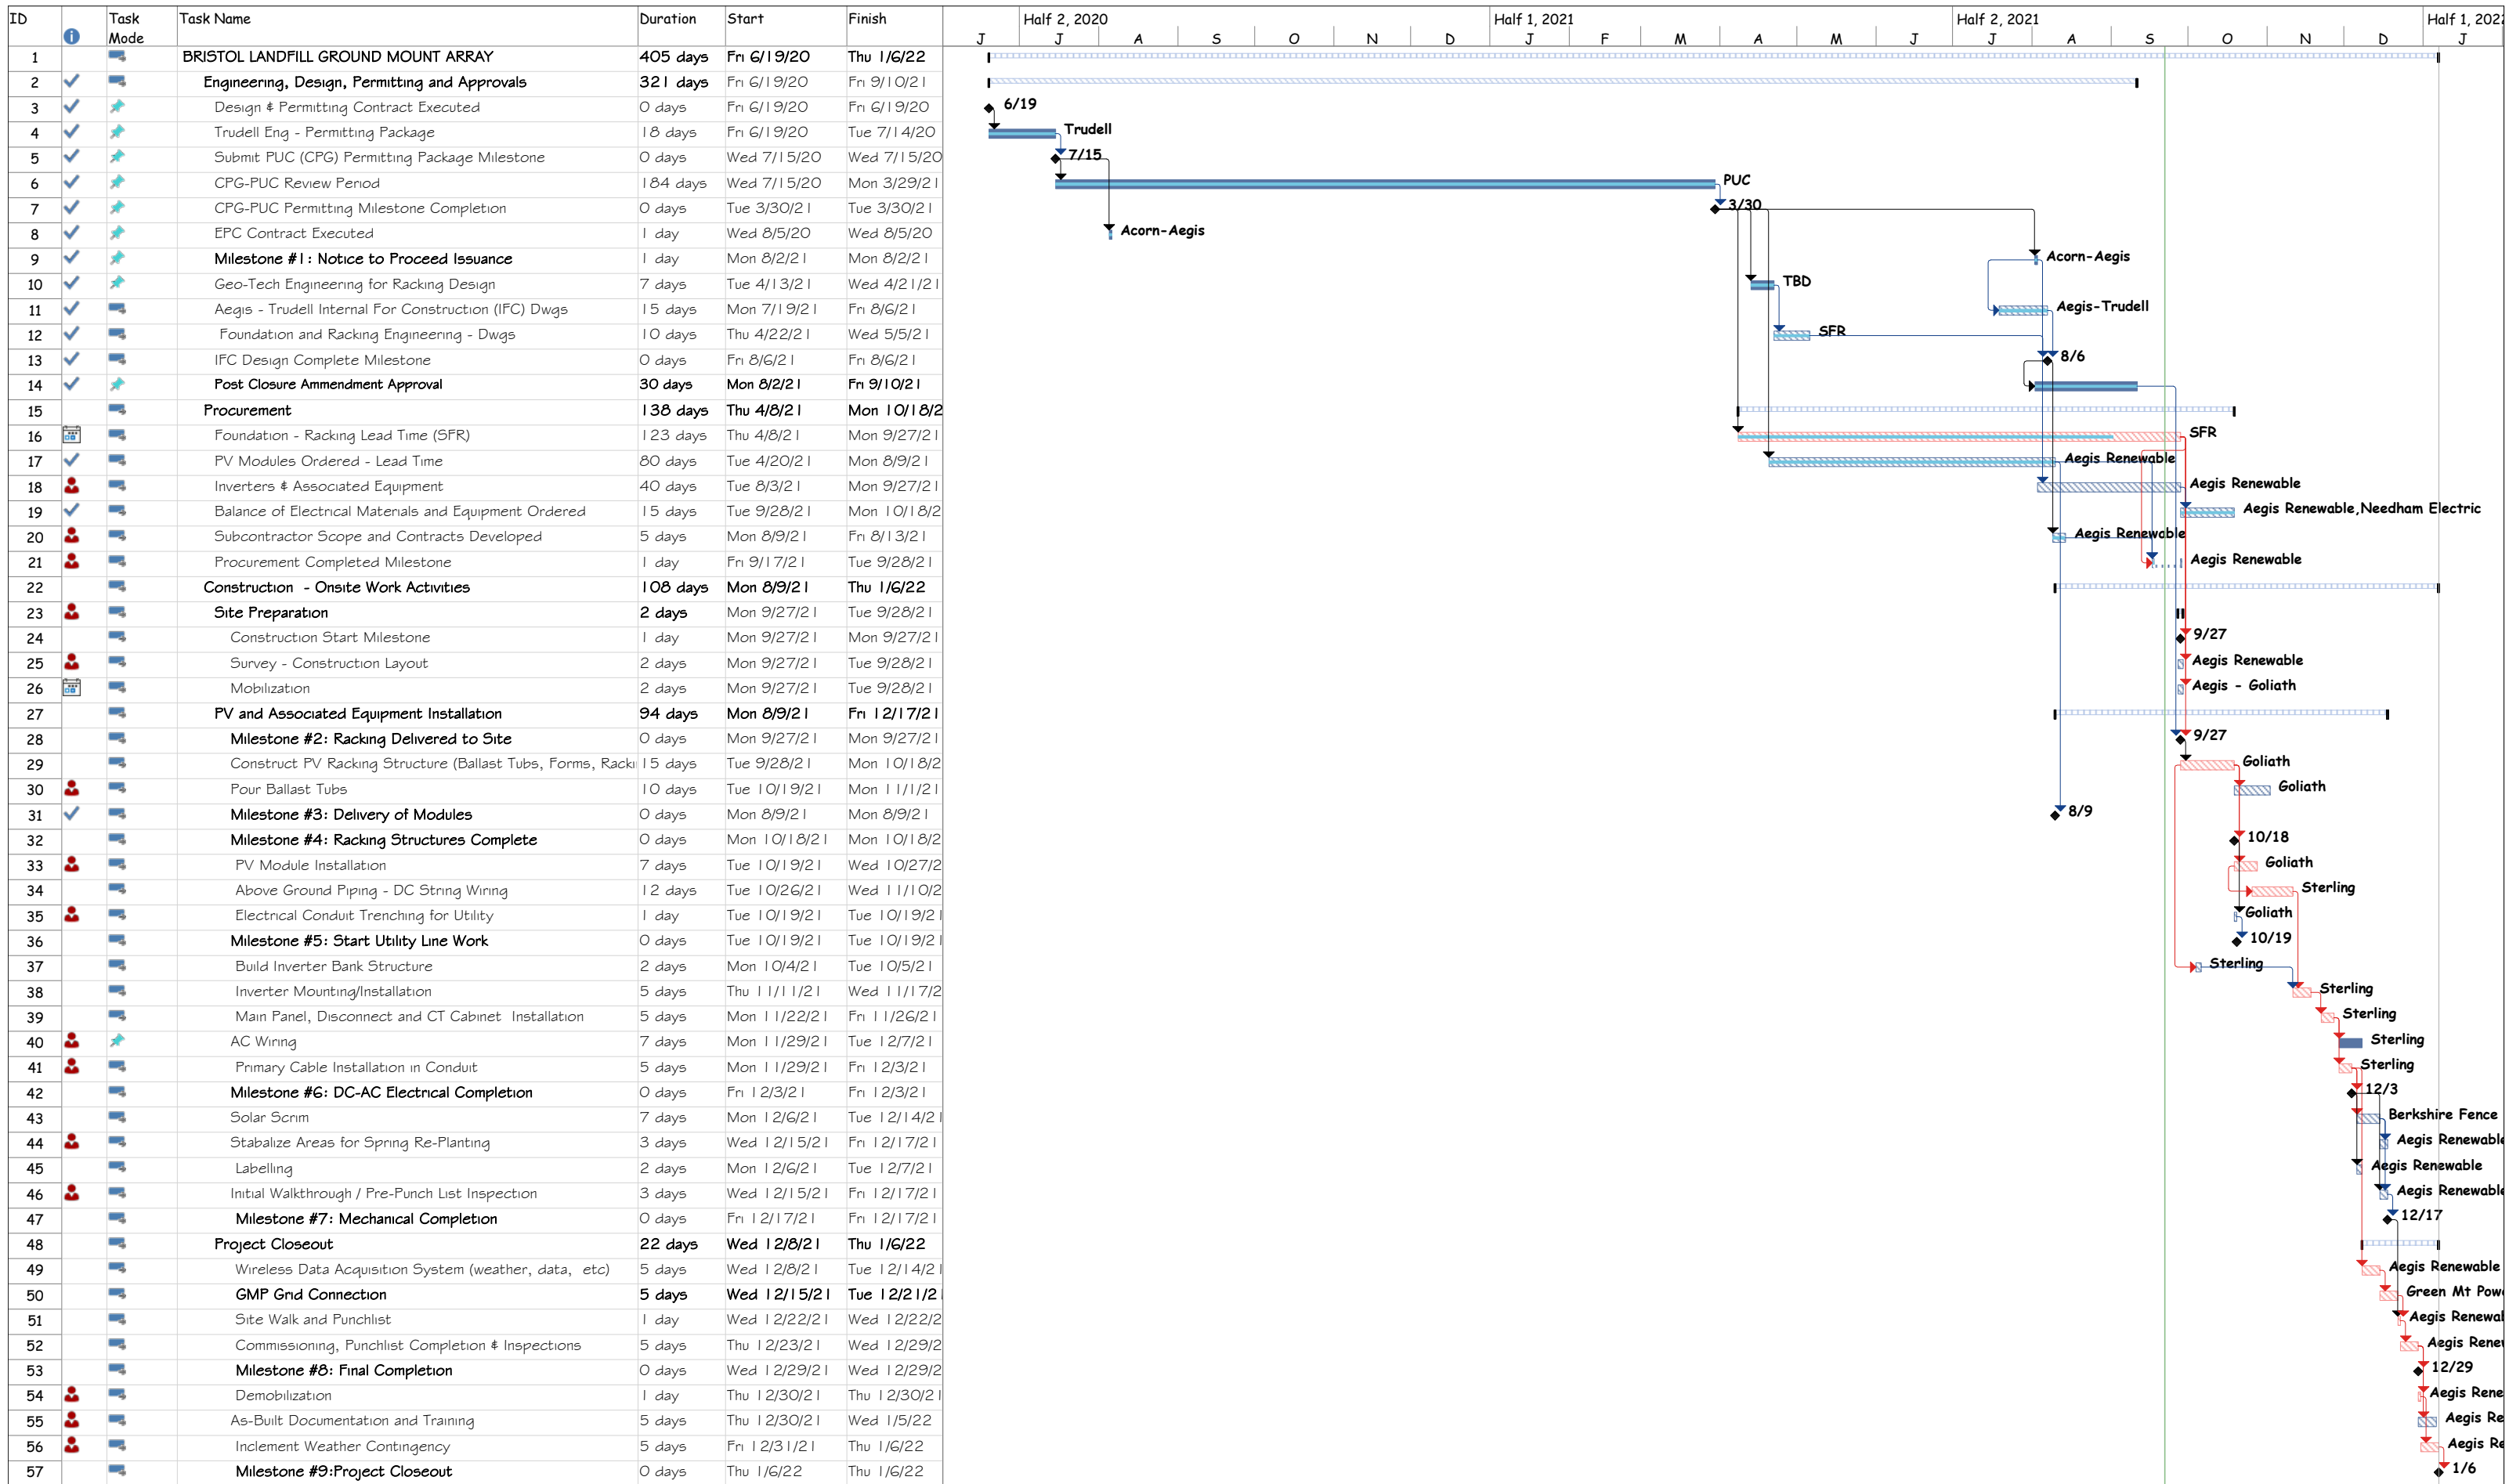

Project: 2021-05-19_BristolLF_S	Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split
Date: Wed 9/22/21	Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress
	Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress
