

Bristol Town Administrator

From: Nick Morehouse <nmorehouse@aegis-re.com>
Sent: Saturday, November 6, 2021 10:43 AM
To: Ben Marks; Bristol Town Administrator
Cc: Eric Cota; Richard Butz; Greg Pahl; Richard Carpenter; Tom Dunne; Susan Smiley; Peter Carothers; Sally Burrell; Thomas Flynn; Eric Phaneuf; Nils Behn; Sonia Behn; Nick Morehouse
Subject: Acorn Bristol Solar Project Status Report 10
Attachments: 2021-11-05_Acorn Bristol_Status_Report_#10.pptx; 2021-11-01_BristolLF_Schedule_Final_2.3.pdf

Hello Ben & Valerie,

Please find the latest status report and project plan attached. Please let me know if you have any questions. I look forward to seeing some of you at the site Thursday at 9:00.

Be well,
Nick

Nick Morehouse
Senior Project Manager



Aegis Renewable Energy
, Inc.
340 Mad River Park, Suite 6
Waitsfield, VT 05673
Main: [802-496-5155](tel:802-496-5155)
Cell: [802-557-5240](tel:802-557-5240)



The information contained in this facsimile/email transmission is privileged and confidential and is intended only for the use of the recipient listed above. If you are neither the intended recipient or an employee or agent of the intended recipient responsible for the delivery of this information, you are hereby notified that the disclosure, copying, use or distribution of this information is strictly prohibited. If you have received this transmission in error, please notify us immediately to arrange for the return of the transmitted documents or to verify their destruction.



**Bristol 500 kW Ground Mount
Acorn Energy Solar 3, LLC.
Status Report 10
11/05/2021**

Acorn Bristol Solar

Scope Elements	Current Status	Action Items-Look Ahead's-Notes
Permitting	All permits are issued.	
General Conditions	All subcontracts in place.	
Site Work-Excavation	All stone pads completed	Pond & Trenching
Racking	All stone pads are built all ballasts are placed. 164 of 176 ballasts have been filled with concrete. Racking 95% complete.	Scheduled for completion week of 11/8
Electrical Equipment Procurement	All long lead time items have been ordered	
Electrical Equipment (Med Dist)		
Electrical Install		Planned mobilization week of 11/8
PV Modules	33% complete	Scheduled for completion week of 11/8
Inverters		Stored on-site
Data Acquisition System (DAS)		Stored on-site
Fencing		Solar Scrim stored on site
Project Commissioning – Mech Comp		
Utility Work- Interconnection		Expecting a schedule from GMP for the RTU next week.

Current Schedule Performance: **50% ±Complete...** Current Schedule Version: 2021-09-10_BristolLF_Schedule_Final_2.3

Current Project Completion Date (WPS): 12/21/2021



Project Contacts:


Nick Morehouse
Sr. Project Manager
340 Mad River Park, Suite 6
Waitsfield, VT 05673

C: 802.557.5240
nmorehouse@aegis-re.com

Tom Flynn P.E.
COO
340 Mad River Park, Suite 6
Waitsfield, VT 05673

O: 802.496.5155
C: 617-694-8464
tflynn@aegis-re.com

www.aegis-re.com

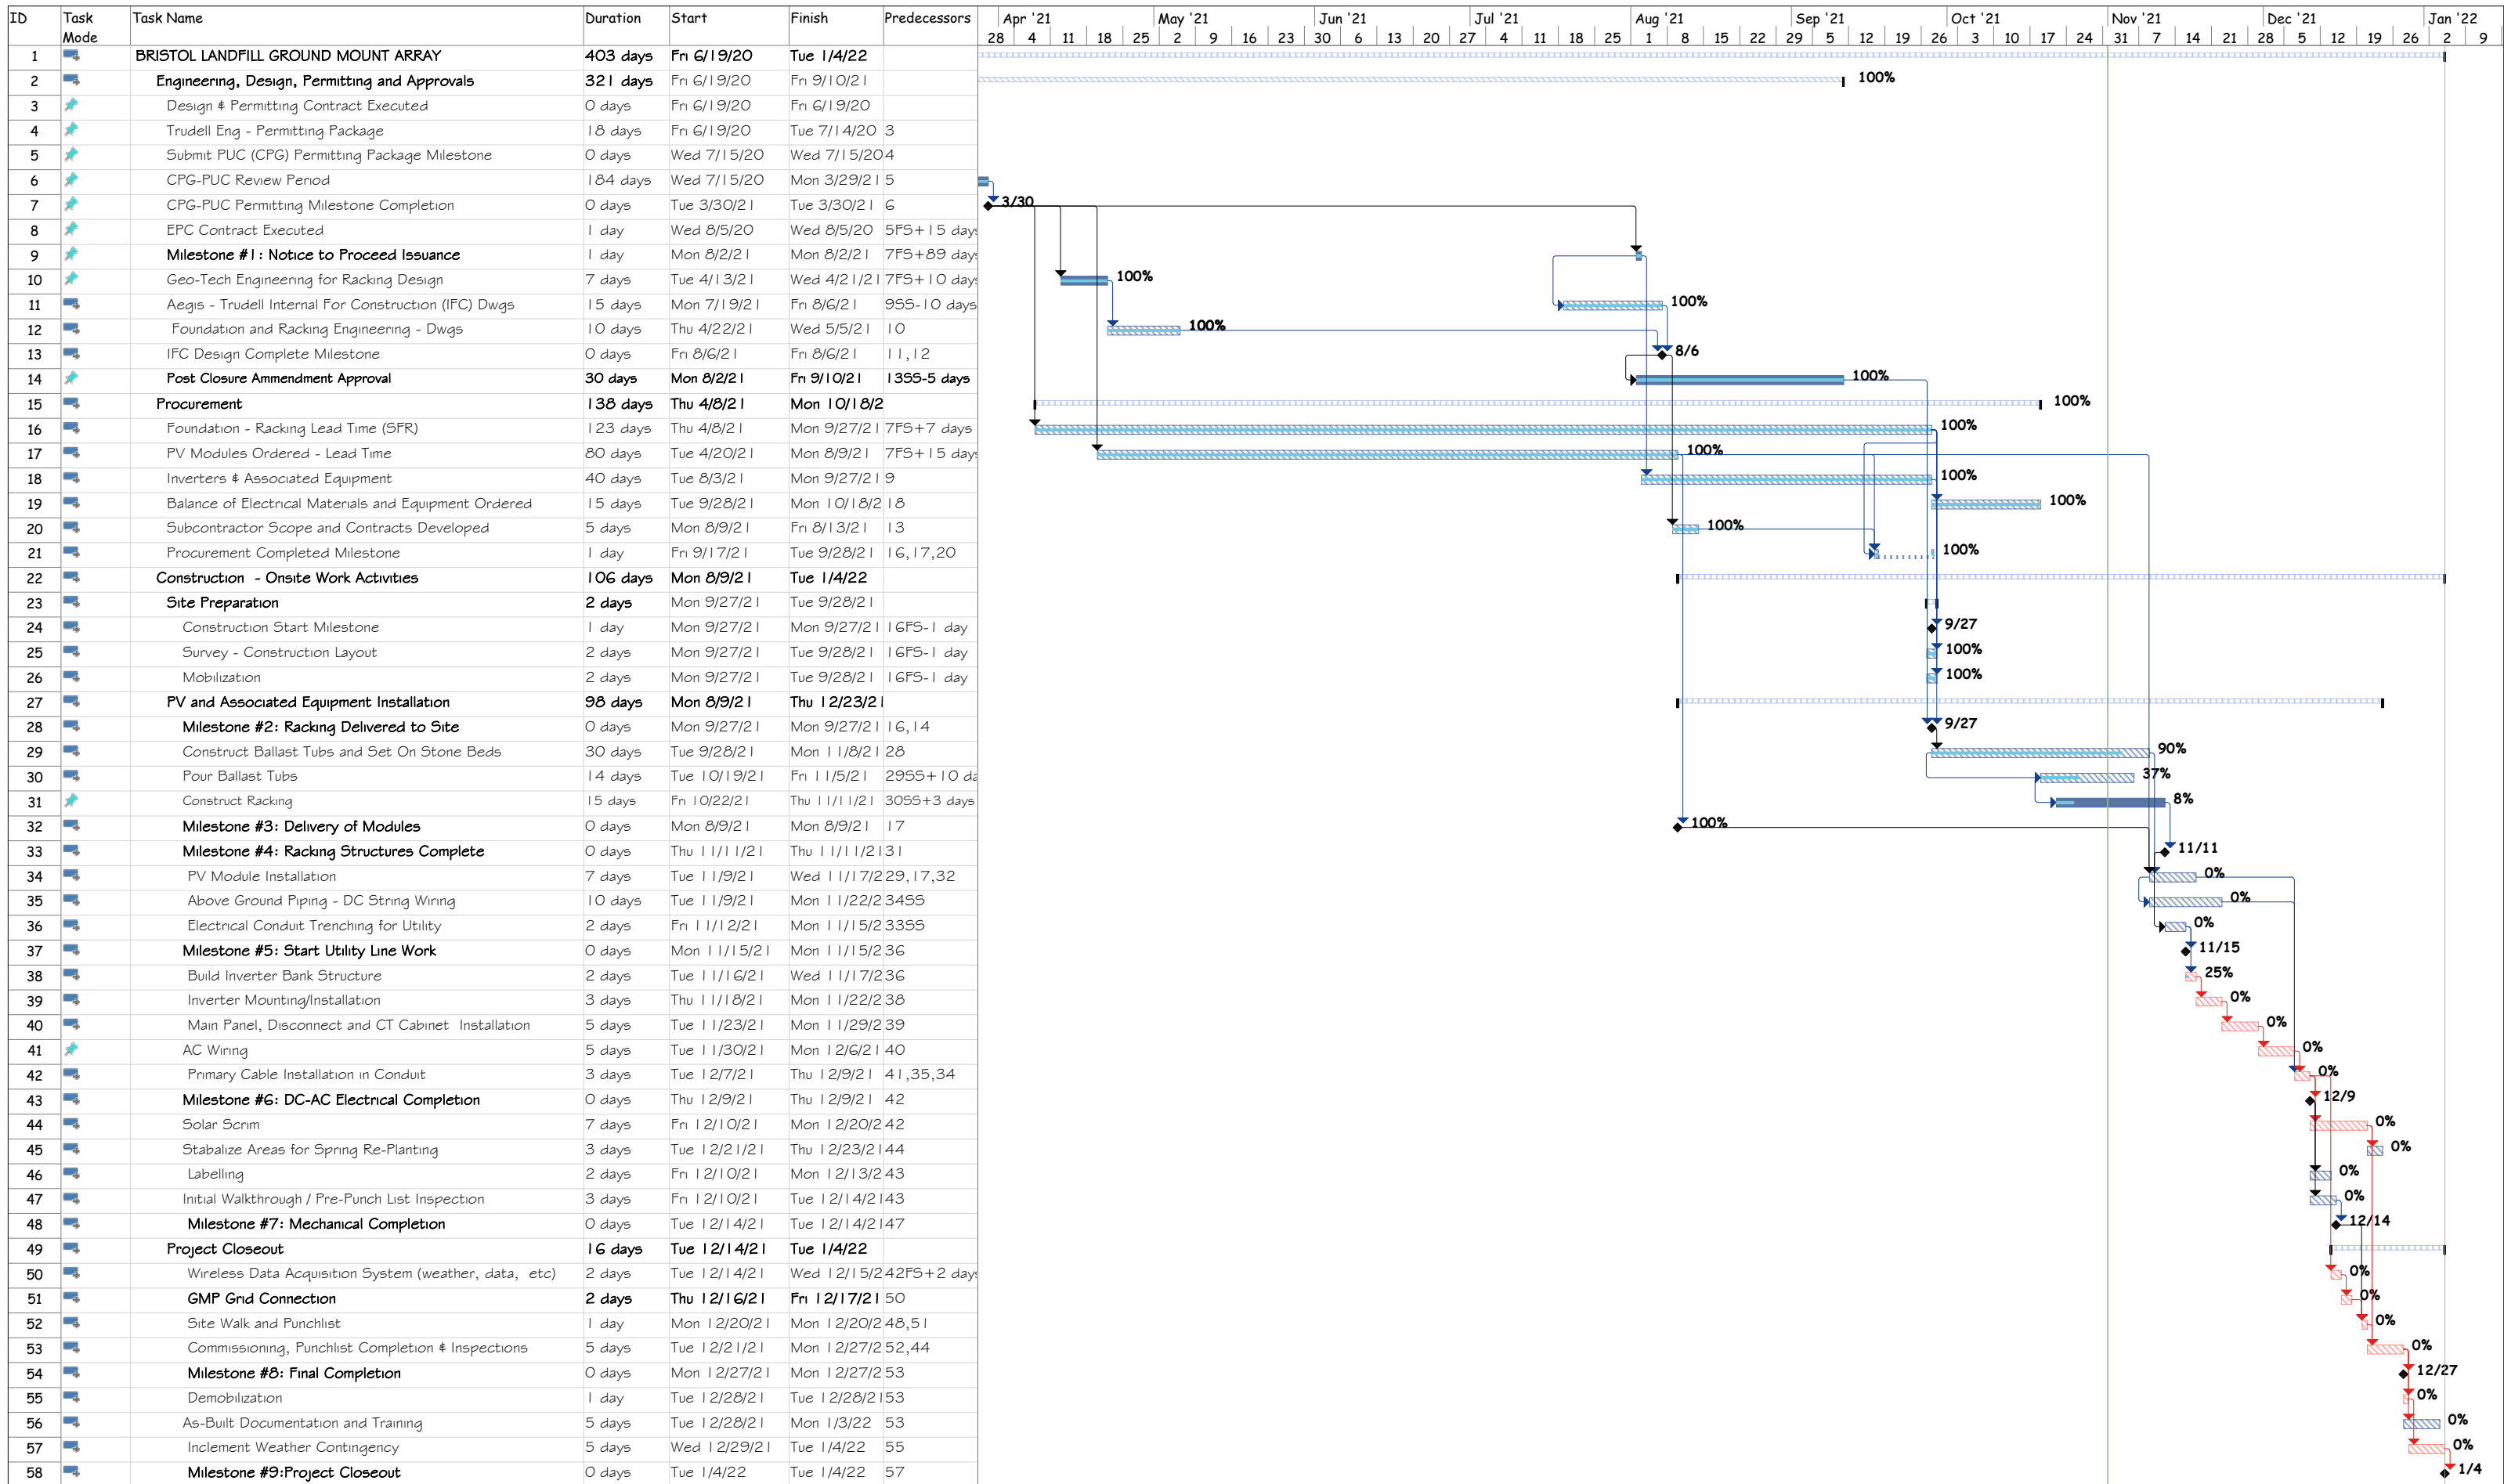

Project: 2021-05-19_BristolLF_S
Date: Mon 11/1/21

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	
